



Additions and Alterations to: Quakertown Community High School Quakertown Community School District



CONSTRUCTION: WORK COMPLETED TO DATE

Project meetings were held with the contractors on July 11, 2016, and July 25, 2016. The meetings were held at the project trailer behind the High School.

Continuing to review Contractor work and providing support to the Architect.

The General Contractor continues to hold weekly coordination meetings at the project trailer.

The following materials were received:
Drywall for Phase 3B
Metal Framing for Phase 3B
Insulation for Phase 3B

Architect has Prepared Unit I punch lists. School District provided Furniture scheduled to be delivered beginning August 8, 2016

The General Contractor performed the following work:
Misc. punch list items-ongoing and SCI punch lists
Form/pour sidewalks south parking lot
Installation of rain screen I/F
Form/pour brick shelf infill J
Final coat paint I1
Final clean I1
Hang doors I1
Install lockers I1
Interior glass install I1
Completion of fume hood enclosures
Install automated door opener
Install card reader bollard I
Interior/exterior demo unit F
Demo J exterior/interior
Interior/exterior framing unit F
Demo sidewalks at unit G/H
Continue storm sewer south parking lot

Sequence of Work for Construction:

Phase 3A

June 2015 to
August 2016

Phase 3B-1

June 2016 to
August 2016

Phase 3B-2

August 2016 to
December 1, 2016

Phase 4

June 2016 to
August 2017

Phase Detailed descriptions on
Page 4





Science Lab

**CONSTRUCTION:
WORK COMPLETED TO DATE (CONT'D.)**

Plumbing Contractor performed the following:

- In wall rough-in Art Room complete
- FCS casework complete
- Demo gas and water mains Unit J-1
- Started underground Unit J-1
- Started overhead rain water F-1

HVAC Contractor performed the following:

- Continue coordination with GC, EC & PC
- Continued Daily Clean-up
- Continue Demo
- Install Silencer in the TV Studio
- Install Ductwork in the Art Rooms
- Continue Building Automation (Controls)

The Electrical Contractor performed the following:

- Demo Unit J section 1st and 2nd floor and lower level basement
- Overhead and in wall rough in F section
- Completed data testing Unit I section
- Installing remaining fixtures lower level basement
- Installed and tested all fixtures and devices digital editing



Unit J—2nd Floor

The Balancing Contractor:

- Continues to perform air and water balancing.
- Supporting Commissioning activities

Abatement Contactor:

- Ceilings in Unit J Completed.
- Continue demo Unit J 1st and 2nd Floors



Unit J—1st Floor

DECISIONS REQUIRED

Abatement Change Orders—Floor in the Art Room

CRITICAL ISSUES

None at present.



South Side Exterior
Unit J

WORK TO COMPLETE NEXT 30 DAYS



**Art Room Looking
at Kiln Room**



**Art Room
Mechanical Closet**



Dance Studio



**Display Cases
At Art Rooms**

General Contractor

- Continue with work listed above
- Install shoring for west end of J second floor/roof
- Install roofing area F
- Boiler room steel infill
- Install additional drying racks lower level G
- Complete Glazing
- Complete thresholds
- Unit I punch list
- Use and Occupancy Inspection

Plumbing Contractor:


- Continue underground Lower F
- Complete casework in FCS
- Complete relocation of 2" gas service
- Start rough-in F-1
- Continue demo of existing water main Lower C, B

HVAC Contractor:

- Continue Demo
- Continue Art Room Ductwork.
- Reinstall HVAC Units
- Continue Building Automation (Controls)

Electrical Contractor:

- Continue:
 - Demo J section 1st and 2nd floor and lower level basement
 - Overhead and in wall rough in F section
 - Completed data testing I section
 - Installing remaining fixtures lower level basement
 - Installed and tested all fixtures and devices digital editing
 - Wattstopper Activation and programming
 - Electrical Inspection

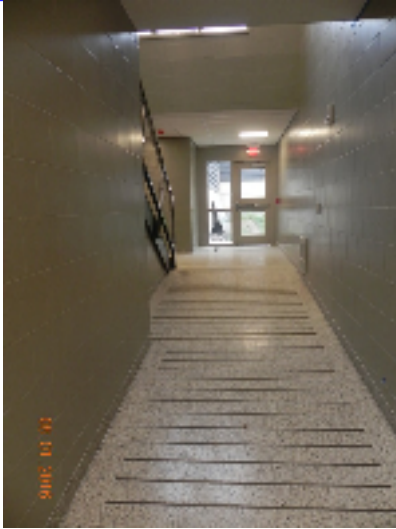

Unit I Ramp

MAJOR SCHEDULE EVENTS

Phase 3A - Major Rooms Completion August 14, 2016

- First Floor Unit I
 - Conference Room
 - 1 Special Ed Room
 - Locker Lobby
 - 1 Computer Room
 - 6 Classrooms
 - 2 FCS Classrooms
 - Restrooms
- Second Floor
 - 5 Science Labs
 - 4 Science Classrooms
 - 1 Faculty Room
 - Restrooms

Phase 3B-1 - Major Rooms Completion August 14, 2016

- First Floor
 - 2 Art Rooms

Phase 3B-2 - Major Rooms Completion December 1, 2016

- First Floor
 - 2 Tech Ed Rooms
 - Dance Studio

Phase 4 - Major Rooms Completion August 2017

- First Floor
 - 10 Classrooms
 - 1 IPC
 - 1 Seminar Room
 - 1 IT Closet
 - 1 Electrical Closet
- Second Floor
 - 3 Physics Labs
 - 7 Classrooms
 - 1 IPC
 - 1 Seminar Room
 - 1 Electrical Closet



Unit I -Stairs



1st Floor
Unit i -Corridor



Unit I -Stairs
